Month-end asks one question.
Do these records describe the same work?

Schedule, cost and package records can each be credible while leaving their scope relationships unclear.



Schedule

Delivery sequence



Cost / Forecast

Control accounts



Work Packages


Commercial scope

Establish the relationship before drawing the management conclusion.

WBS↔LINK

Three sources. One owner reference.

Owner Work Breakdown Structure (WBS): relate sources while keeping their evidence and authority distinct.

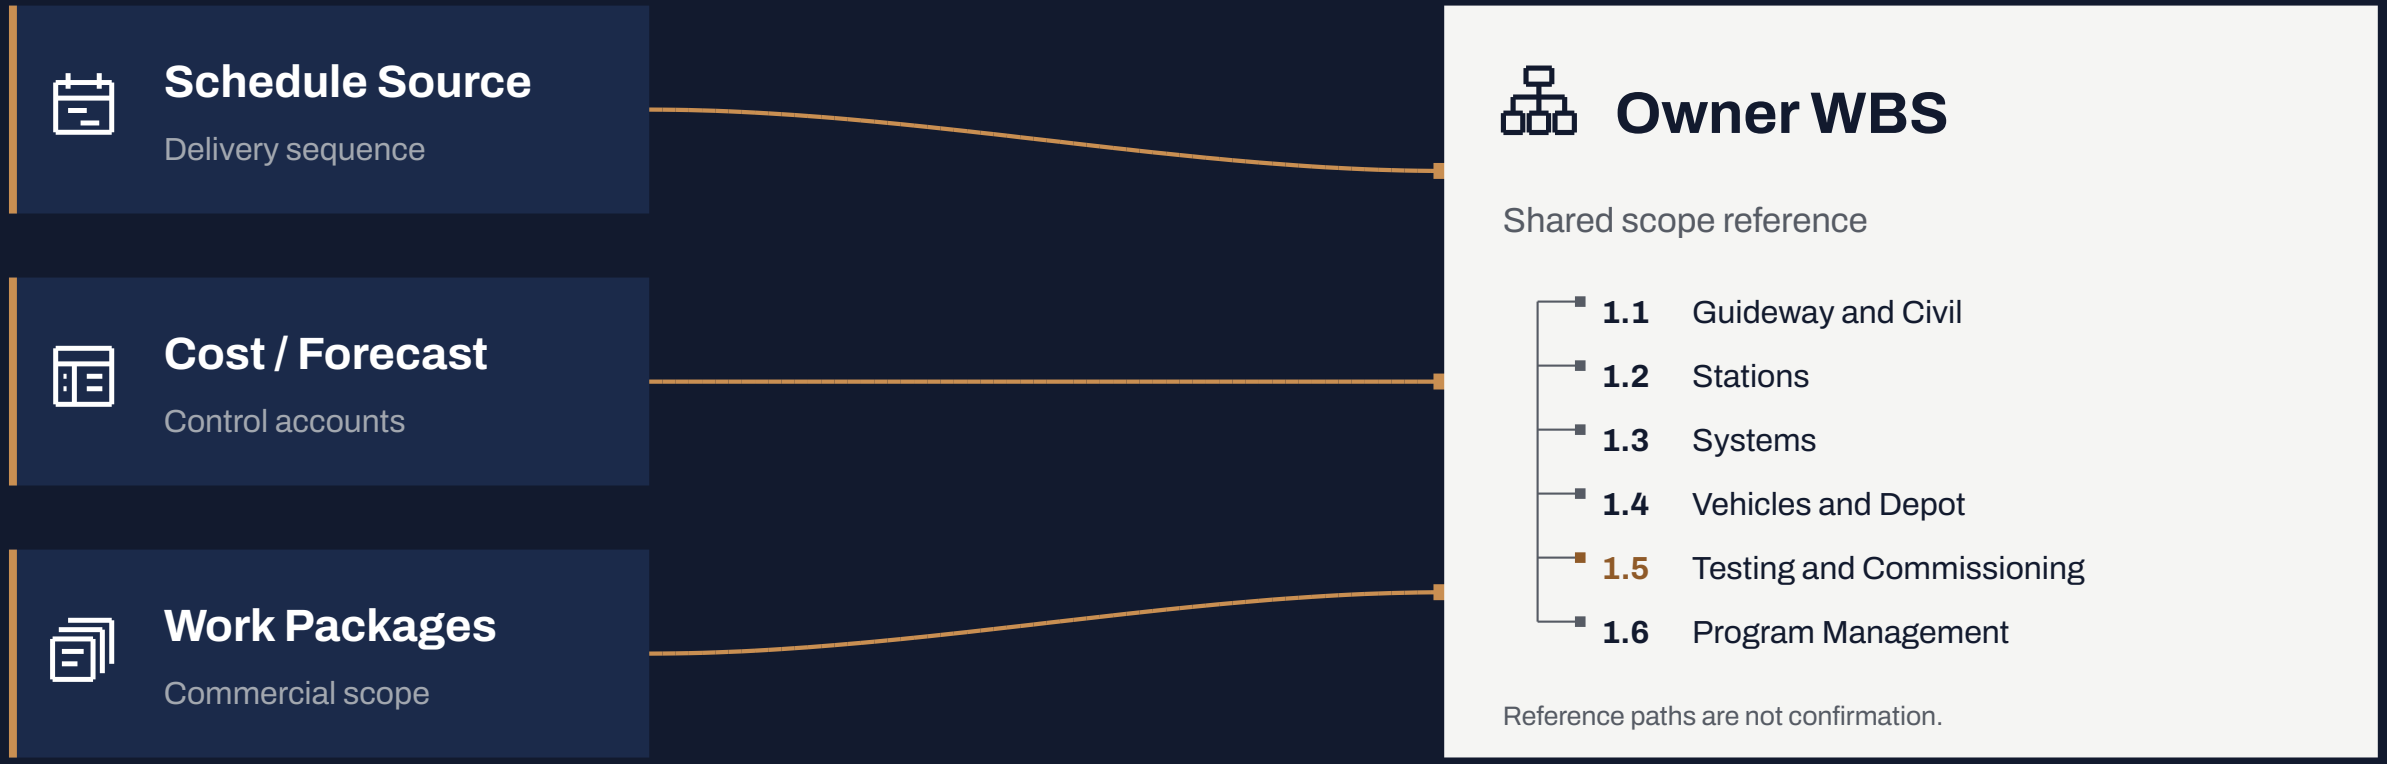

RELATIONSHIP OUTCOMES REMAIN DISTINCT

Source-backed
Evidence preserved

Gap visible
Not forced into WBS

Human review
Decision scope recorded

Method illustration. Sources remain separate; no automatic confirmation, progress claim or merged dataset.

What the source says is separate from what was decided.

Professional interpretation and whole-version approval have different scopes.



Original evidence

Source assertions remain inspectable. An original code is not individual confirmation.



Professional decision

The record states who decided, which relationships and what uncertainty remains.



Separate approval

Structure approval and reporting approval are distinct. Neither authorizes payment.

Approval of a version does not individually validate every source relationship.

A schedule view exists. The cost relationship does not.

Testing and Commissioning needs a governed relationship review.

OWNER WBS 1.5

Testing and Commissioning

180

schedule relationships

ABSENT

0 cost relationships

Not a zero-cost claim

EXACT PROFESSIONAL ACTION

Confirm whether the missing governed relationship is expected or requires project-controls attention.

Actual July source position. A coverage gap establishes neither missing work nor schedule impact.

Evidence: F-0611c8162d / SCH-05-001 / original assertion: WBS Code = 1.5.1

Source assignment is not individually reviewed. Whole-version approval remains separate.

July added an unresolved package relationship.

A reporting change calls for review. Its cause and project impact are not established.

Unresolved relationships

263 to **264**

Unresolved package relationships

0 to **1**

The same two work-area gaps remain. Program Management cost relationships: 80 to 79.

1,622 current relationships in both cycles. July: 3 retired historical versions; 1,625 versions in all.

Follow one finding.
Then test your own judgement.

Read the recorded July example before making independent synthetic practice decisions.



Finding + exact Action



Original source



Decision scope



Separate approval

Read the July HarbourLink finding

Recorded report and “Try the app” are different journeys. Use synthetic data only.
