HarbourLink Urban Transit Expansion

1. The approved information position

Version 2 · Maya Chen, Owner Project Controls. Whole-version approval remains separate from individual review.

4 of 6	1,622	264	1,623
areas with both views	current mapping records	unresolved	current target rows

1.1 Project Connections through Owner WBS

Owner WBS work area	Schedule	Cost	Packages
1.1 Guideway and Civil	**181**	**81**	**9**
1.2 Stations	**180**	**80**	**12**
1.3 Systems	**179**	**79**	**10**
1.4 Vehicles and Depot	**179**	**80**	**10**
1.5 Testing and Commissioning	**180**	**Not found**	**10**
1.6 Program Management	**Not found**	**79**	**9**

Distinct mapped source versions within each work area. A split connection can appear in more than one area. Do not sum branches as project totals. The mapping-record total above also includes unresolved and outside-WBS outcomes.

1.2 Professional attention

Confirm whether the missing governed relationship is expected or requires project-controls attention.

Use only conclusions that do not depend on these unresolved relationships.

Cost / forecast totals remain withheld. Relationship coverage is not progress, project health or a financial position.

Since the previous approved cycle: unresolved 263 → 264; outside Owner WBS 1 → 0; no applicable WBS 1 → 1.

2. Findings and exact professional Actions

Schedule and cost coverage differ in this WBS area

1.5 Testing and Commissioning

The schedule has an established relationship to this Owner WBS area, but cost does not.

Exact governed Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

Cost and schedule coverage differ in this WBS area

1.6 Program Management

Cost has an established relationship to this Owner WBS area, but the schedule does not.

Exact governed Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

264 items still need more information before they can be placed in the Owner WBS

The approved project view keeps them unresolved instead of forcing them into a WBS area.

Exact governed Action

Use only conclusions that do not depend on these unresolved relationships.

04 ISSUES FOR REVIEW → 08 CROSSWALK (Relationship Type filter) → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

3. Where source review remains

3.1 Original source outcomes

Commercial Package Register

59 related / 0 outside/no WBS / 1 unresolved



Contractor Programme

899 related / 1 outside/no WBS / 182 unresolved



Cost & Forecast Control Accounts

399 related / 0 outside/no WBS / 81 unresolved



Each current relationship is counted once. Solid: related; light: outside/no applicable WBS; patterned: unresolved.

3.2 Open outcomes remain distinct



1,622 current relationships. Retired versions excluded; split targets counted once. These outcomes do not rank financial exposure or risk.


4. The reporting-cycle position

4.1 Movement since the previous approved version

1,613
carried forward

1
re-keyed, revalidated

3
retired versions

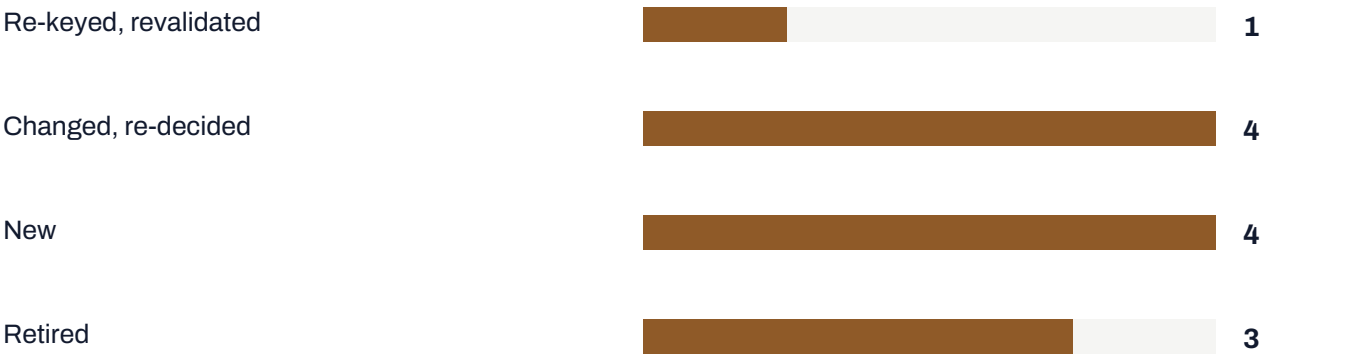

Detail scale excludes 1,613 carried-forward versions. All change classes total 1,625, including retired. 1,614 remained valid under their recorded classifications; neither class means every source assertion was individually confirmed.

Population	Current	Including history
Distinct relationship versions	1622	1625
Target rows	1623	1626

Recorded movement does not establish cause, responsibility, schedule delay, financial exposure or deadline. Inspect Changes & Revalidation for the original scope and decision basis.

5. Locate the original evidence

5.1 / 1.5 Testing and Commissioning

Source: Contractor Programme

Record / relationship: SCH-05-001 / R721-v2

Original assertion: WBS Code = 1.5.1

Contrary evidence: None recorded; absence is not independent validation.

Basis / professional decision: Source assignment -- not individually reviewed / No individual decision scope recorded / No individual decision-maker recorded

Revision / period: Rev 1 / Contractor Programme Cycle 2

Inspect this finding and its workbook route

5.2 / 1.6 Program Management

Source: Cost & Forecast Control Accounts

Record / relationship: CST-06-001 / R1483-v2

Original assertion: Cost Account = CA-6001; WBS Code = 1.6.1

Contrary evidence: None recorded; absence is not independent validation.

Basis / professional decision: Source assignment -- not individually reviewed / No individual decision scope recorded / No individual decision-maker recorded

Revision / period: Rev 1 / Cost & Forecast Control Accounts Cycle 2

Inspect this finding and its workbook route

5. Source evidence / continued

5.3 / 264 items still need more information before they can be placed in the Owner WBS

Source: Cost & Forecast Control Accounts

Record / relationship: CST-03-004 / R1246-v3

Original assertion: Cost Account = CA-3004

Contrary evidence: None recorded; absence is not independent validation.

Basis / professional decision: Earlier professional decision, carried forward / Group decision (81 records sharing one decision state), carried forward / Maya Chen, Owner Project Controls

Revision / period: Rev 1 / Cost & Forecast Control Accounts Cycle 2

Inspect this finding and its workbook route

6. Reporting authority and evidence routes

Approved at 2026-10-16 14:14:10.063502 by Maya Chen, Owner Project Controls. Source reporting dates: Data date: 2026-07-31 (Contractor Programme Rev 1); 2026-07-31 (Cost & Forecast Control Accounts Rev 1); 2026-07-31 (Commercial Package Register Rev 1). Approval records are retained as fictional attribution, not independently verified identities.

09 WBS Explorer counts distinct relationships for scope navigation. 14 WBS Hierarchy counts target rows, including split/retired rows unless filtered. Use 08 Crosswalk → 10 Evidence & Decisions → 11 Sources & Provenance. Exact source fingerprints and historical rows remain in the Premium Workbook.

Source assertions, software interpretation, contrary evidence, professional decision and approval remain separate. Agreement between outputs does not validate source meaning.
