HarbourLink Urban Transit Expansion

1. Approved baseline. Review the coverage gaps.

Version 1 · Maya Chen, Owner Project Controls. Whole-version approval remains separate from individual review.

> Initial approved baseline. No earlier approved cycle is available for comparison.

4 of 6
areas with both views

263
unresolved records

1.1 Where management attention is needed

Inspect work areas with a missing Schedule or Cost view. A missing relationship limits the information position; it does not establish that work or expenditure is absent.

Owner WBS work area	Schedule	Cost	Packages
1.1 Guideway and Civil	**180**	**80**	**10**
1.2 Stations	**179**	**80**	**11**
1.3 Systems	**180**	**79**	**10**
1.4 Vehicles and Depot	**179**	**80**	**10**
1.5 Testing and Commissioning	**180**	**Not found**	**10**
1.6 Program Management	**Not found**	**80**	**10**

1.2 Exact professional Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

Review the governed NEW_SCOPE outcomes in the project-controls context.

Use only conclusions that do not depend on these unresolved relationships.

Cost / forecast totals remain withheld. Coverage is not progress, project health or a financial position. Branch counts can overlap; do not sum them. Missing connections require review, not assumed zero values.

2. Findings and exact professional Actions

Schedule and cost coverage differ in this WBS area

1.5 Testing and Commissioning

The schedule has an established relationship to this Owner WBS area, but cost does not.

Exact governed Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

Cost and schedule coverage differ in this WBS area

1.6 Program Management

Cost has an established relationship to this Owner WBS area, but the schedule does not.

Exact governed Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

1 item is recorded outside the current Owner WBS

Outside the current Owner WBS

The approved project view records work that the current Owner WBS does not represent.

Exact governed Action

Review the governed NEW_SCOPE outcomes in the project-controls context.

04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

263 items still need more information before they can be placed in the Owner WBS

The approved project view keeps them unresolved instead of forcing them into a WBS area.

Exact governed Action

Use only conclusions that do not depend on these unresolved relationships.

04 ISSUES FOR REVIEW → 08 CROSSWALK (Relationship Type filter) → 10 EVIDENCE & DECISIONS

Evidence and authority → supporting record

3. Where source review remains

3.1 Original source outcomes

Commercial Package Register

60 related / 0 outside/no WBS / 0 unresolved



Contractor Programme

898 related / 2 outside/no WBS / 182 unresolved




Cost & Forecast Control Accounts

399 related / 0 outside/no WBS / 81 unresolved



Each current relationship is counted once. Solid: related; light: outside/no applicable WBS; patterned: unresolved.

3.2 Open outcomes remain distinct

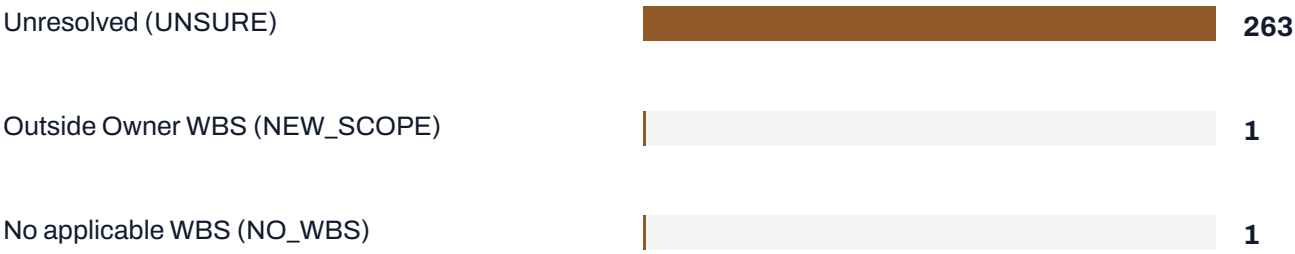

1,622 current relationships; 1,623 governed export / outcome rows, including targetless outcomes. Retired versions excluded; split targets counted once. These outcomes do not rank financial exposure or risk.

4. The reporting-cycle position

4.1 Initial approved baseline

1,622
initial approved relationships

No prior cycle
comparison withheld

The New classification establishes the first baseline. It is not growth relative to an earlier approval.

4.2 Source reporting dates

Original source	Reporting date	Revision
Owner WBS	2026-06-30	Rev 0
Contractor Programme	2026-06-30	Rev 0
Cost & Forecast Control Accounts	2026-06-30	Rev 0
Commercial Package Register	2026-06-30	Rev 0

4.3 A separate approval event

Version 1 was approved at 2026-10-16 14:11:18.493651 by Maya Chen, Owner Project Controls.

Source reporting dates describe the information basis. Approval time records a separate governance event. Neither is evidence of installed progress, payment entitlement or individual confirmation of every assertion.

Recorded movement does not establish cause, responsibility, schedule delay, financial exposure or deadline. Inspect Changes & Revalidation for the original scope and decision basis.

5. Locate the original evidence

5.1 / 1.5 Testing and Commissioning

Source: Contractor Programme

Record / relationship: SCH-05-001 / R721-v1

Original assertion: WBS Code = 1.5.1

Contrary evidence: None recorded; absence is not independent validation.

Basis / professional decision: Source assignment -- not individually reviewed / No individual decision scope recorded / No individual decision-maker recorded

Revision / period: Rev 0 / Initial

Inspect this finding and its workbook route

5.2 / 1.6 Program Management

Source: Cost & Forecast Control Accounts

Record / relationship: CST-06-001 / R1483-v1

Original assertion: Cost Account = CA-6001; WBS Code = 1.6.1

Contrary evidence: None recorded; absence is not independent validation.

Basis / professional decision: Source assignment -- not individually reviewed / No individual decision scope recorded / No individual decision-maker recorded

Revision / period: Rev 0 / Initial

Inspect this finding and its workbook route

5. Source evidence / continued

5.3 / Outside the current Owner WBS

Source: Contractor Programme

Record / relationship: SCH-90-901 / R1081-v2

Original assertion: WBS Code = 2.1

Contrary evidence: Source states 'WBS Code' = '2.1' -- names no element of this WBS -- professional reason (Maya Chen, Owner Project Controls): Source states a project-delivery code outside the currently approved Owner WBS.

Basis / professional decision: Professional decision / Individual / Maya Chen, Owner Project Controls

Revision / period: Rev 0 / Initial

Inspect this finding and its workbook route

5.4 / 263 items still need more information before they can be placed in the Owner WBS

Source: Cost & Forecast Control Accounts

Record / relationship: CST-03-004 / R1246-v2

Original assertion: Cost Account = CA-3004

Contrary evidence: None recorded; absence is not independent validation.

Basis / professional decision: Professional decision / Group decision (81 records sharing one decision state) / Maya Chen, Owner Project Controls

Revision / period: Rev 0 / Initial

Inspect this finding and its workbook route

6. Financial source quotations · no aggregate position

These are literal source assertions, not an approved financial position or allocated child costs. Whole source account, not a target allocation. Repeated target rows must not be summed. Aggregate cost / forecast remains withheld.

Record / relationship: CST-01-001 / R1083-v1

Source / location: monthly_cost_forecast.xlsx / Supplied practice file monthly_cost_forecast.xlsx, row 2

Source budget / forecast: 347500 / 347500

Currency / dedicated basis: CAD / Not supplied (not zero)

Source as of / revision: 2027-06-30 / C1-R0

Record / relationship: CST-01-003 / R1085-v1

Source / location: monthly_cost_forecast.xlsx / Supplied practice file monthly_cost_forecast.xlsx, row 4

Source budget / forecast: 382500 / 407500

Currency / dedicated basis: CAD / Not supplied (not zero)

Source as of / revision: 2027-06-30 / C1-R0

Record / relationship: CST-01-005 / R1087-v1

Source / location: monthly_cost_forecast.xlsx / Supplied practice file monthly_cost_forecast.xlsx, row 6

Source budget / forecast: 417500 / 417500

Currency / dedicated basis: CAD / Not supplied (not zero)

Source as of / revision: 2027-06-30 / C1-R0

Showing 3 of 480 current financial source records. Use 08 CROSSWALK → Whole-source budget / forecast for every recorded value, currency, basis, date and revision. Blank source values remain unavailable, not zero.

7. Reporting authority and evidence routes

Approved at 2026-10-16 14:11:18.493651 by Maya Chen, Owner Project Controls. Source reporting dates: Data date: 2026-06-30 (Contractor Programme Rev 0); 2026-06-30 (Cost & Forecast Control Accounts Rev 0); 2026-06-30 (Commercial Package Register Rev 0). Approval records are retained as fictional attribution, not independently verified identities.

09 WBS Explorer counts distinct relationships for scope navigation. 14 WBS Hierarchy counts target rows, including split/retired rows unless filtered. Use 08 Crosswalk → 10 Evidence & Decisions → 11 Sources & Provenance. Exact source fingerprints and historical rows remain in the Premium Workbook.

Source assertions, software interpretation, contrary evidence, professional decision and approval remain separate. Agreement between outputs does not validate source meaning.
