WBS↔LINK™

ZP SYNERGY GROUP INC.

HarbourLink Urban Transit Expansion

Integrated Management Report

Cycle update

Reporting basis: Version 2 · confirmed by Maya Chen, Owner Project Controls · 2026-10-12 14:28 UTC

Data date: 2027-07-31 (Contractor Programme Rev 1); 2027-07-31 (Cost & Forecast Control Accounts Rev 1); 2027-07-31 (Commercial Package Register Rev 1)

Candidate for controlled synthetic review

Print, phone and responsive browser present the same approved findings, exact Actions, evidence and withholding.

Open Executive Summary →

Contents

One approved position. A complete evidence route.

S01 · Executive Summary

S02 · WBS Coverage and Gaps

S03 · Source Relationship Outcomes

S04 · Reporting-Cycle Movement

S05 · Professional Actions and Evidence

S06 · Evidence and Assurance

Read the coverage pattern first; choose a finding; follow its own source and professional decision; compare the next approved cycle.

Workbook index: 02 START HERE. Primary scope view: 09 WBS EXPLORER. Advanced scope/relationship-row analysis remains accessible.

S01 · Executive Summary

Reporting basis: Version 2 · confirmed by Maya Chen, Owner Project Controls · 2026-10-12 14:28 UTC

Cost / forecast total withheld. Aggregation eligibility is not established. Full qualifications appear in S06.

4 / 6

reported Owner-WBS branches have both schedule and cost relationships

E01 · Named branch coverage

Coverage through the Owner WBS; not project health or direct schedule-to-cost equivalence.

1.1 Guideway and Civil

Schedule: ✓ Present · Cost: ✓ Present

1.2 Stations

Schedule: ✓ Present · Cost: ✓ Present

1.3 Systems

Schedule: ✓ Present · Cost: ✓ Present

1.4 Vehicles and Depot

Schedule: ✓ Present · Cost: ✓ Present

1.5 Testing and Commissioning

Schedule: ✓ Present · Cost: Absent

1.6 Program Management

Schedule: Absent · Cost: ✓ Present

Takeaway: 1.5: Cost coverage gap; 1.6: Schedule coverage gap

Issues for review · 3 distinct groups

Issues 1, 2

1.5 Testing and Commissioning; 1.6 Program Management

Professional Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

F-0611c8162d → S05 · F-7a4c154c28 → S05

Issues 3

264 items still need more information before they can be placed in the Owner WBS

Professional Action

Use only conclusions that do not depend on these unresolved relationships.

F-0aaa67f1b0 → S05

Meaningful reporting-cycle change

1,613 carried forward; 1 re-keyed/revalidated. Together 1,614 of 1,625 relationships remained valid under the recorded change classification; denominator includes retired relationships.

Withheld

A management total is not included because the supplied information does not establish all of the measure, currency, period, record-grain and allocation rules needed to aggregate it reliably.

S02 · WBS Coverage and Gaps

E01 · Branch relationship counts

Distinct governed relationships within each reported branch. A split relationship can appear in more than one branch.

1.1 Guideway and Civil

Schedule: 181 · Cost: 81 · Both views present

1.2 Stations

Schedule: 180 · Cost: 80 · Both views present

1.3 Systems

Schedule: 179 · Cost: 79 · Both views present

1.4 Vehicles and Depot

Schedule: 179 · Cost: 80 · Both views present

1.5 Testing and Commissioning

Schedule: 180 · Cost: 0 · Cost coverage gap

1.6 Program Management

Schedule: 0 · Cost: 79 · Schedule coverage gap

Coverage through the Owner WBS; not project health or direct schedule-to-cost equivalence.

Availability means at least one governed relationship is present. Absence is bounded to the supplied source set and approved relationship state; it does not establish missing project scope or financial materiality.

Evidence route: 05 INTEGRATION HEALTH → 09 WBS EXPLORER → 08 CROSSWALK

S03 · Source Relationship Outcomes

E02 · Where records are placed

1,622 current relationships (retired excluded)

Commercial Package Register

Total: 60

Related to a WBS element: 59

Recorded outside the WBS: 0

Left unresolved: 1

Shared zero-based E02 scale: 0 to 1,082 distinct relationships. Current, retired excluded.

Contractor Programme

Total: 1,082

Related to a WBS element: 899

Recorded outside the WBS: 1

Left unresolved: 182

Shared zero-based E02 scale: 0 to 1,082 distinct relationships. Current, retired excluded.

Cost & Forecast Control Accounts

Total: 480

Related to a WBS element: 399

Recorded outside the WBS: 0

Left unresolved: 81

Shared zero-based E02 scale: 0 to 1,082 distinct relationships. Current, retired excluded.

Distinct Relationship IDs; split targets count once per source. 03 EXECUTIVE VIEW source table → 08 CROSSWALK → 10 EVIDENCE & DECISIONS.

E04 · Unresolved and outside-WBS outcomes

Left unresolved on purpose (UNSURE): 264

Scope not in the approved WBS (NEW_SCOPE): 0

No WBS element applies (NO_WBS): 1


1,622 current relationships (retired excluded)

Unresolved is not assessed outside scope; NO_WBS and NEW_SCOPE remain separate outcomes.

S04 · Reporting-Cycle Movement

1,613 carried forward; 1 re-keyed/revalidated. Together 1,614 of 1,625 relationships remained valid under the recorded change classification; denominator includes retired relationships.

E03 · Whole population · zero-based scale

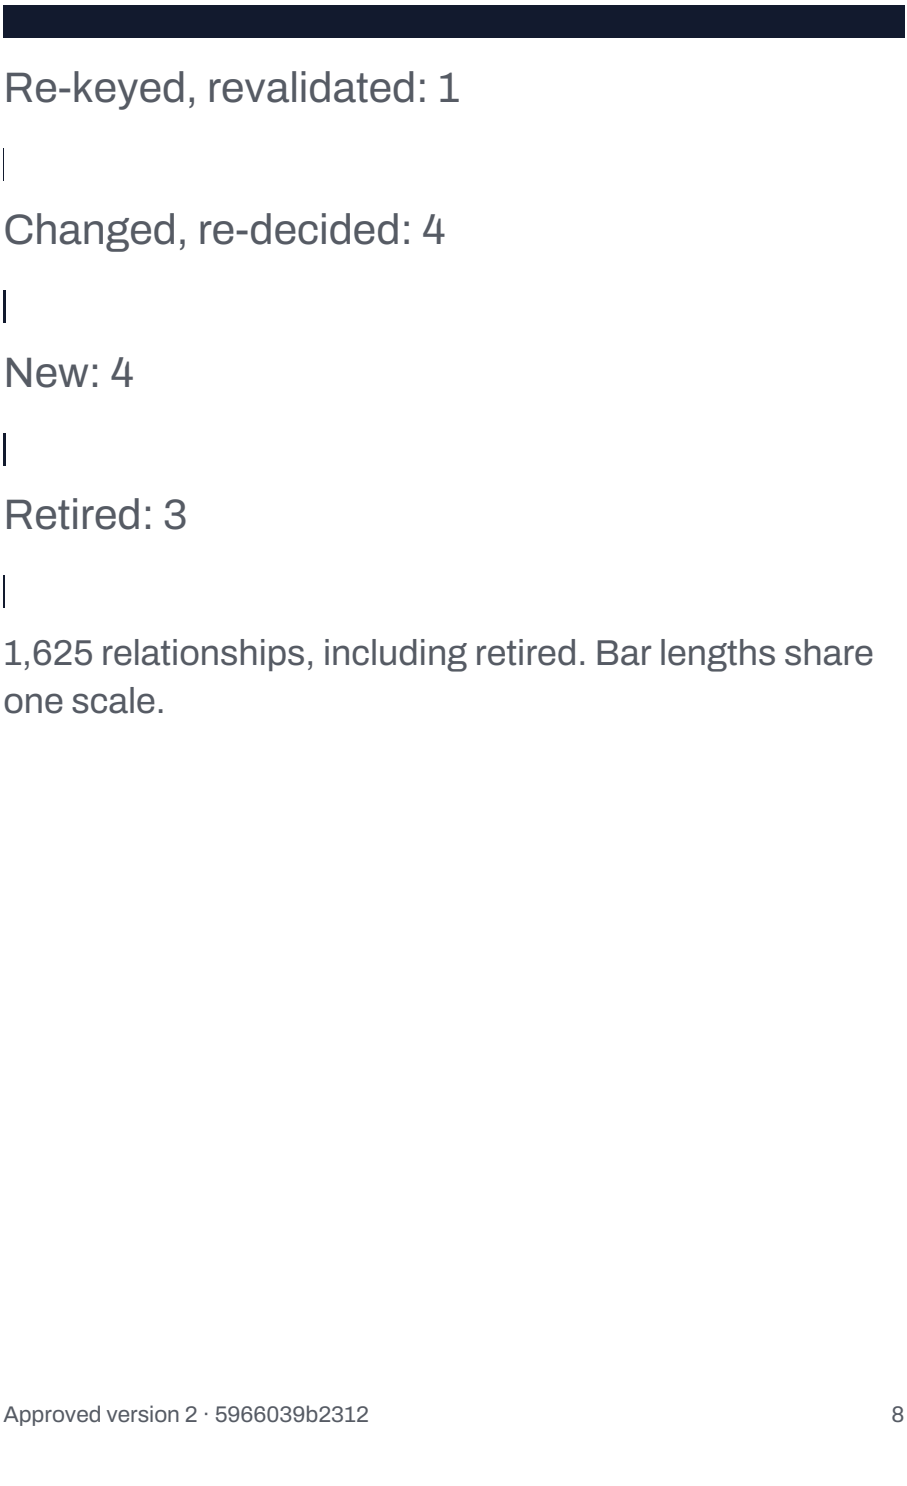

1,625 relationships, including retired. Bar lengths share one scale.

E03D · Small movement classes

Separate detail scale; Carried forward excluded. Counts and zero-based lengths remain exact.

Re-keyed, revalidated: 1

[redacted]

Changed, re-decided: 4

[redacted]

New: 4

[redacted]

Retired: 3

[redacted]

07 CHANGES & REVALIDATION → 13 REVISIONS & PERIODS → stable Relationship ID in 08 CROSSWALK.

Current non-carried-forward relationships exclude retired and include revalidation; changed/new/retired includes retired and excludes revalidation.

S05 · Professional Actions and Evidence

F-0611c8162d

1.5 Testing and Commissioning

The schedule has an established relationship to this Owner WBS area, but cost does not.

Professional Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

Source Record ID SCH-05-001 · Relationship ID R721-v2

Gap basis: 1.5 has schedule 180 and cost 0 governed relationships. This record illustrates the present view; the absent view is established by the bounded branch population, not this record alone.

1 · Original source assertion

WBS Code = 1.5.1

2 · Interpretation and contrary evidence

ONE_TO_ONE → 1.5.1 Testing and Commissioning - Test Readiness
Contrary source evidence: None recorded.
Evidence note: None recorded.

3 · Relationship basis

Source assignment -- not individually reviewed
No individual named decision recorded.
Decision scope: Not recorded for this record.

4 · Separate approval authority

MappingVersion 2
Approved by: Maya Chen, Owner Project Controls
Recorded (UTC): 2026-10-12 14:28:24.403730

Original source: Contractor Programme · Rev 1 · Contractor Programme Cycle 2 · Central section: test procedure readiness review - field start

Workbook: 04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Return to Executive Summary

F-7a4c154c28

1.6 Program Management

Cost has an established relationship to this Owner WBS area, but the schedule does not.

Professional Action

Confirm whether the missing governed relationship is expected or requires project-controls attention.

Source Record ID CST-06-001 · Relationship ID R1483-v2

Gap basis: 1.6 has schedule 0 and cost 79 governed relationships. This record illustrates the present view; the absent view is established by the bounded branch population, not this record alone.

1 · Original source assertion

Cost Account = CA-6001; WBS Code = 1.6.1

2 · Interpretation and contrary evidence

ONE_TO_ONE → 1.6.1 Program Management - Program Controls
Contrary source evidence: None recorded.
Evidence note: None recorded.

3 · Relationship basis

Source assignment -- not individually reviewed
No individual named decision recorded.
Decision scope: Not recorded for this record.

4 · Separate approval authority

MappingVersion 2
Approved by: Maya Chen, Owner Project Controls
Recorded (UTC): 2026-10-12 14:28:24.403730

Original source: Cost & Forecast Control Accounts · Rev 1 · Cost & Forecast Control Accounts Cycle 2 · Program Management - design integration - professional services

Workbook: 04 ISSUES FOR REVIEW → 09 WBS EXPLORER → 08 CROSSWALK → 10 EVIDENCE & DECISIONS

Return to Executive Summary

F-0aaa67f1b0

264 items still need more information before they can be placed in the Owner WBS

The approved project view keeps them unresolved instead of forcing them into a WBS area.

Professional Action

Use only conclusions that do not depend on these unresolved relationships.

Source Record ID CST-03-004 · Relationship ID R1246-v3

1 · Original source assertion

Cost Account = CA-3004

2 · Interpretation and contrary evidence

UNSURE → UNSURE
Contrary source evidence: None recorded.
Evidence note: None recorded.

3 · Recorded professional decision

Earlier professional decision, carried forward
Decided by: Maya Chen, Owner Project Controls
Decision scope: Group decision (81 records sharing one decision state), carried forward

4 · Separate approval authority

MappingVersion 2
Approved by: Maya Chen, Owner Project Controls
Recorded (UTC): 2026-10-12 14:28:24.403730

Original source: Cost & Forecast Control Accounts · Rev 1 · Cost & Forecast Control Accounts Cycle 2 · Systems - systems integration - professional services

Workbook: 04 ISSUES FOR REVIEW → 08 CROSSWALK (Relationship Type filter) → 10 EVIDENCE & DECISIONS

Return to Executive Summary

S06 · Evidence and Assurance

Source assertions, software interpretation, contrary evidence, professional decision and approval remain separate. Agreement between outputs does not validate source meaning.

Approved MappingVersion 2 · WBS version 1

Approved by: Maya Chen, Owner Project Controls
Recorded (UTC): 2026-10-12 14:28:24.403730

09 WBS EXPLORER: relationship coverage/status. 14 WBS HIERARCHY: relationship ROWS, including split targets and retired rows unless filtered.

Owner WBS · Rev 0 · WBS dictionary

Contractor Programme · Rev 1 · schedule

Cost & Forecast Control Accounts · Rev 1 · cost estimate

Commercial Package Register · Rev 1 · work-package list

Withheld

A management total is not included because the supplied information does not establish all of the measure, currency, period, record-grain and allocation rules needed to aggregate it reliably.

Review boundaries

Fictional synthetic evaluation; no real-client provenance is implied. Loading the recorded example does not approve uploaded user data. No client-data, security, compliance, financial-materiality or hosting-residency assurance is implied.
